


Project Brief



Project: LMS 002

Project manager	Ikeije Adanna	
Client	UK-based School	
Accountable officer	Uche Ubani	
Project ID	LMS-ALM-UK-002	
Version / Date revised	1.0	28. 01. 2026

Revision history

Version	Date	Author	Summary of changes
1.0	28.01.2026	Uche Ubani	Initial version
1.1	02.02.26	Uche Ubai	Program Managers correction implemented on details.

1. Project Description

a. Current Situation & Background

The client is a UK-based school that currently relies heavily on manual processes and paper-based systems to manage academic, administrative, and operational activities. These activities include student records, staff management, payments, achievements, internal recruitment, and reporting.

Due to the volume of paperwork involved, the school experiences challenges such as:

- Difficulty tracking student and staff activities
- Delays in administrative processes
- Increased risk of errors and lost documentation
- Limited visibility into operational inefficiencies

In today's digital era, educational institutions are increasingly adopting Learning Management Systems (LMS) to centralise operations, improve transparency, and enhance service delivery. A web-based LMS will allow the school to automate processes, provide real-time access to information, and improve collaboration among staff, students, and administrators.

b. Rationale for Project

- To replace inefficient manual processes with a centralised digital system
- To improve administrative efficiency and reduce paperwork
- To provide staff and students with faster, easier access to information
- To identify and resolve operational flaws early through improved data visibility
- To provide team members with real-world project delivery experience in a structured environment

c. Strategic objective this project is aligned to and how

- Increase organisational efficiency
- Profit maximisation and improved Return on Investment (ROI)
- Strengthen internal school management processes
- Improve quality of service delivery for staff and students
- Support digital transformation within the education sector

2. Resource

People (PM, BA, Program Manager, Software developer, Software tester)

2.1 What departments do you think might be involved in making your idea happen? Please indicate in the table below.

	Departments Involved	Services Involved	Other organisations involved
	Finance	Payment tracking, budgeting and fee management.	Payment service providers
	IT/ IS	System security, data protection, Information security Policies and General security management, GDPR compliance. Regular security audits, and compliance with industry standards. Regularly update software and employ a web application firewall	Hosting Providers
	HR	Staff records and recruitment management	
	Academic Administration	Student records, achievements and, reporting	
	Operations	Process coordination and documentation	
	Technical	Software development, testing and deployment	
	Development	Managing client expectations and Market research	
	Portfolio Team (PM, BA, PO)	Project planning and delivery	Almond
	Communications	Plan stakeholder Communications, updates and set communication expectations.	
	L&D	Training users on the LMS	

	Procurement	Negotiating Contract and managing procurement process.	
--	-------------	--	--

2.2 What staffing resources will it require?

People (PM, APM, BA, PO, Software Developer, Software Tester, Program manager)

3. Outcomes

3.1 What difference will this project make to the organisation?

The successful delivery of the LMS will result in:

1. Improved operational efficiency
2. Reduced administrative workload
3. Centralised data management
4. Enhanced transparency and accountability
5. Improved decision-making through reporting and tracking
6. Long-term cost savings
7. Better compliance with record-keeping standards

3.2 What difference will this project make to our customers?

Staff and students will benefit from:

1. Faster access to information
2. Reduced delays in administrative processes
3. Improved communication and coordination
4. Easier tracking of achievements and payments
5. Self-service capabilities
6. Improved user experience
7. Increased satisfaction and engagement

The LMS will simplify day-to-day school interactions and significantly reduce dependency on manual paperwork

4. Estimated Cost

The delivery of the project is estimated to cost £120,000

5. Options

a. Options (do nothing, do minimal or do something)

- **Do Nothing:** Continue with manual, paper-based systems
- **Do Minimal:** Digitise limited records without system integration
- **Do Something:** Develop a full-featured web-based LMS

b. Recommended Option

Do Something – Development of a web-based Learning Management System with the following MVP features:

- Admin user accounts
- Jobs and careers module
- Achievements management
- Payments management
- Search and filtering functionality
- Secure authentication
- User-friendly interface
- GDPR-compliant data handling.

This option provides the highest long-term value and supports scalability

6. Procurement

a. Re-tender or New Solution Idea

Procurement not applicable

b. Current Supplier & Term of Contract

No current Supplier.

7. Outputs & Benefits

Outputs	Expected Benefit or Dis-benefit
• Admin account management • Jobs and careers module • Achievements tracking • Payment management • Search and filter functionality • Centralised LMS platform	• Secure system access • Internal recruitment efficiency • Recognition and transparency • Accurate fee tracking • Faster access to information • Increased efficiency and ROI

8. Scope

In Scope	Out of Scope
• Admin user authentication and profile management • Jobs and careers management • Achievements management • Payments tracking and adjustments • Search and filtering across LMS data • Web-based LMS MVP delivery	• Mobile application development • Advanced analytics and AI features • Post-launch maintenance beyond MVP • Parent portal (future phase)

9. Key Risks, Issues & Mitigation

Key Risk / Issue	Impact	Mitigation
Data security breaches	Data loss or unauthorised access	Encryption, secure authentication, GDPR compliance

Resource unavailability	Schedule delays	Assign backup resources
Scope creep	Budget/time overruns	Strict change control
Limited user adoption	Reduced value	User training and engagement

10. Project Governance

10.1 Stakeholder Map

Partner: Almond, Program manager

Engage: PMs, Developers, Testers, BAs

Consult: School Management, Finance, IT, HR

Inform: School staff and students

Consult School Management	Engage: Finance	Engage BAs	Engage/Partner: Almond media Program Manager PM	Engage/Partner: PMs Developer Software Tester BA
Consult: HR / IT	Engage	Engage PMO	Engage	Engage
Consult In	Consult	Engage	Engage	Engage
Inform "	Inform	Consult	Engage	Engage
Inform	Inform	Consult	Consult	Consult

High

High


10.2 Roles and Responsibilities

Name	Role	Responsibilities
------	------	------------------

Tolu Dada	Accountable Officer	Project delivery, coaching of the team and project vision.
School Management	Client	Funding and approvals
Developers	Developers	System Development
Processing Bank	Payment Processing	Payment Processing
Ikeije Adanna	Project Manager	Project delivery
Tester	Software Tester	Quality Assurance

1.

10.3 Project Management Team Structure

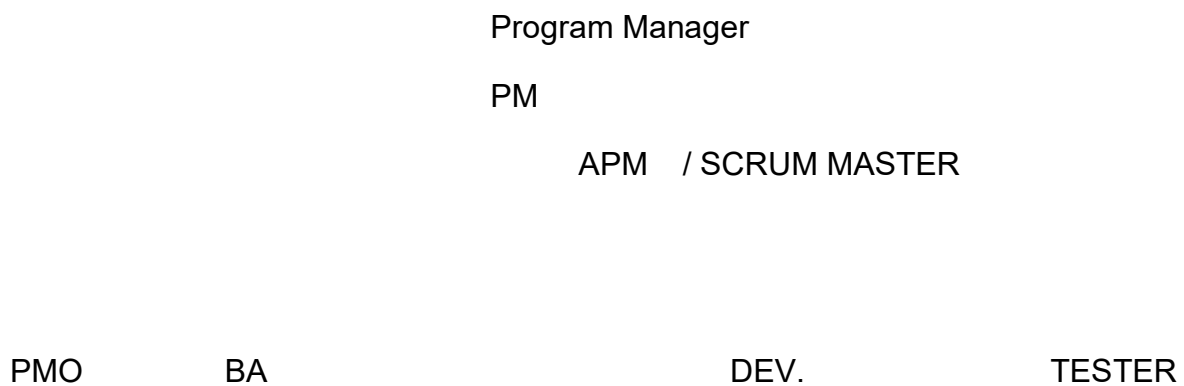

10.4 Project Controls

We have a project plan that consists of managing different aspects of the project that includes; time, cost, quality, scope and communication. There will also be a baseline against which the project will be managed.

- **Time:** Weekly milestone tracking
- **Cost:** Budget monitoring and reporting
- **Quality:** Testing against requirements
- **Scope:** Change requests via Product Owner
- **Communication:** Weekly team and stakeholder updates

11. Breakdown of Costs

11.1 Breakdown by Year

Year of spend	Amount	Description of spend (Revenue cost, Capital cost, Savings Generated)
2026	£120,000	Development and delivery

11.2 Source of Funding

School Budget.

11.3 Benefits vs Costs

The long-term efficiency gains, reduced administrative costs, and improved service delivery outweigh the initial investment, delivering strong ROI.

12. Plan

12.1 Expected Project Start, Go-Live & Close Dates

Start Date	Go-Live Date	Close Date
11.01.2026	20.04.2026	20.04.2026

12.2 High Level Project Timeline

	Week											
	1	2	3	4	5	6	7	8	9	10	11	12
Initiation												
Planning												
Design												
DevGrooming and Planning												
Dev Sprints												
Closure												

12.3 Key Milestones

Stage	Key Milestone	Due Date
-------	---------------	----------

Project Initiation	Kick off meeting	12.01.2026 (WEEK 1)
Planning	Requirements gathering	Week 3 - 4
Design	Design and development	Week 5 - 7
Dev Sprints	Testing	Week 8 - 11
Delivery	MVP completion / Closure	20.04.2026 (WEEK 12)

13. Sign offs

Please submit to the Portfolio Office once complete and retain receipt for your records.

If submitting through Procurement, approved by:

Delegated Authority	Click here to enter text.
---------------------	---
